

TOWN OF FORT FRANCES

OPERATIONS & FACILITIES DIVISION

BUILDING PERMIT APPRAISAL

| | |
|---|---|
| CHECKED BY: <u>T. LAW</u> | DATE: <u>OCTOBER 16, 2014</u> |
| ADDRESS (of new construction): <u>118 THIRD STREET WEST</u> | |
| NAME OF DEVELOPER: <u>JACK GREY</u> | |
| ADDRESS OF OWNER/ DEVELOPER: <u>118 THIRD ST. W.</u> | |
| DEVELOPMENT /SUBDIVISION: <u>SINGLE DETACHED DWELLING</u> | |
| EXISTING SANITARY SEWER MAIN: DEPTH: <u>NA</u> | SIZE: <u>380mm</u> MATERIAL: <u>AC</u> |
| EXISTING WATER MAIN: DEPTH: <u>NA</u> | SIZE: <u>150mm</u> MATERIAL: <u>DI</u> |
| EXISTING STORM SEWER MAIN: DEPTH: <u>NA</u> | SIZE: <u>450mm</u> MATERIAL: <u>PVC</u> |
| EXISTING CONNECTION TO PROPERTY: SEWER: <input checked="" type="checkbox"/> WATER: <input checked="" type="checkbox"/> STORM: <u>NA</u> | |

APPLICATION MUST BE MADE TO THE TOWN OF FORT FRANCES PUBLIC WORKS DEPARTMENT FOR EACH OF THE FOLLOWING SERVICES, IF APPLICABLE. THE TOWN OF FORT FRANCES, AT THE DEVELOPERS COST, WILL INSTALL ALL SERVICES. THE APPROPRIATE FORMS FOR EACH SERVICE PROVIDED MUST BE FILLED OUT SIGNED AND DEPOSIT MADE BY THE DEVELOPER BEFORE A BUILDING PERMIT IS ISSUED. IF THE DEVELOPER PLANS TO RECONNECT TO EXISTING SERVICES THE MANAGER OF OPERATIONS AND FACILITIES OR AN APPROVED DESIGNATE WILL BE RESPONSIBLE FOR THE PERFORMING THE INSPECTION. THE EXISTING SERVICES ARE TO BE EXPOSED AT THE PROPERTY LINE BY THE DEVELOPER TO PERMIT THE INSPECTION. THE INSPECTION WILL CONSIST OF VERIFYING THE SIZE, MATERIAL TYPE AND DEPTH OF THE SERVICES. A CLOSED CIRCUIT TELEVISION INSPECTION (CCTV) WILL DETERMINE IF THE PIPE MEETS PRESENT STANDARDS AND WHETHER OR NOT A CONNECTION CAN BE MADE.

| |
|---|
| SANITARY SEWER SERVICE CONNECTION: <u>4" PVC / VCT</u> |
| WATER SERVICE CONNECTION: <u>19mm COPPER</u> |
| STORM SEWER SERVICE CONNECTION: <u>NA</u> |
| PRIVATE CROSSING (CULVERT): <u>NA</u> |
| PRIVATE CROSSING (CONCRETE): <u>EXISTING (MAY REQUIRE NEW INSTALLATION)</u> |
| WEeping TILE SUMP PUMP DISCHARGE (where): <u>FRONT / SIDE YARD</u> |
| BUILDING GRADE: ELEVATION ON SUBDIVISION PLAN: _____ SET BY FIELD CONDITIONS: <input checked="" type="checkbox"/> |
| ROAD TYPE: ASPHALT: <input checked="" type="checkbox"/> SURFACE TREATMENT: _____ GRAVEL: _____ |
| CONCRETE CURB & GUTTER: <input checked="" type="checkbox"/> |
| OPEN DITCH: <u>NA</u> |
| SWALES: <u>SIDE YARD</u> |
| ADDITIONAL COMMENTS: <u>SUMP PUMP MUST PUMP WATER TO SURFACE</u> |

ADDITIONAL INFORMATION:

EXISTING WATER / SEWER SERVICES MUST BE INSPECTED BY PUBLIC WORKS PRIOR TO CONNECTION - @ OWNER'S EXPENSE

OWNER'S SEWER LINE FULL OF ROOTS & REQUIRES REPLACEMENT

GIVEN TO OWNER
PENDING RESULT OF
LETTER TO COUNCIL
DATED OCT 24/14

PREPARED BY: J. LAW SIGNATURE: [Signature]

- OWNER ADVISED
THAT OCCUPANCY

THE UNDERSIGNED HAS READ AND AGREES TO ALL OF THE TERMS AND CONDITIONS AS DESCRIBED IN THIS DOCUMENT

DEVELOPER: Jack Gray SIGNATURE: [Signature]

WILL NOT BE
GRANTED BEFORE
THIS ISSUE IS
RESOLVED

DATE: OCT. 24 / 14 COPY WITH PERMIT: (INITIAL) [Initials]

TOWN OF FORT FRANCES
CCTV INSPECTION REPORT

Line Location: 118 THIRD STREET WEST

Date: SEPT 15, 2014

CCTV Reference #: VIDEO TAPE

Page: 1 of 1

Technician: VEERT

Pipe Cleaned (By/Date): _____

Camera Travel (MH/CO & With/Against Flow): WITH FLOW

Pipe Diameter: 4" Pipe Material: CI/PVC/VCT Pipe Use: SAN Line Type: SERVICE

Start Time: _____

End Time: _____

Other

Information: _____

Chainage/Remarks:

0' - c-top of clo'in basement, 4" CI pipe

0'-18' - roots @ all joints (mats/balls)

18'-27' - 4" PVC section

24' - clo

27' - 4" VCT

31' - slight offset c joint (1/2")

38' - calcite @ top of joint


41' - Calcite @ top of joint

58' - dip (water), offset joint > 1"

59' - rise to main, service connects into MH

Supervisor

Comments: _____

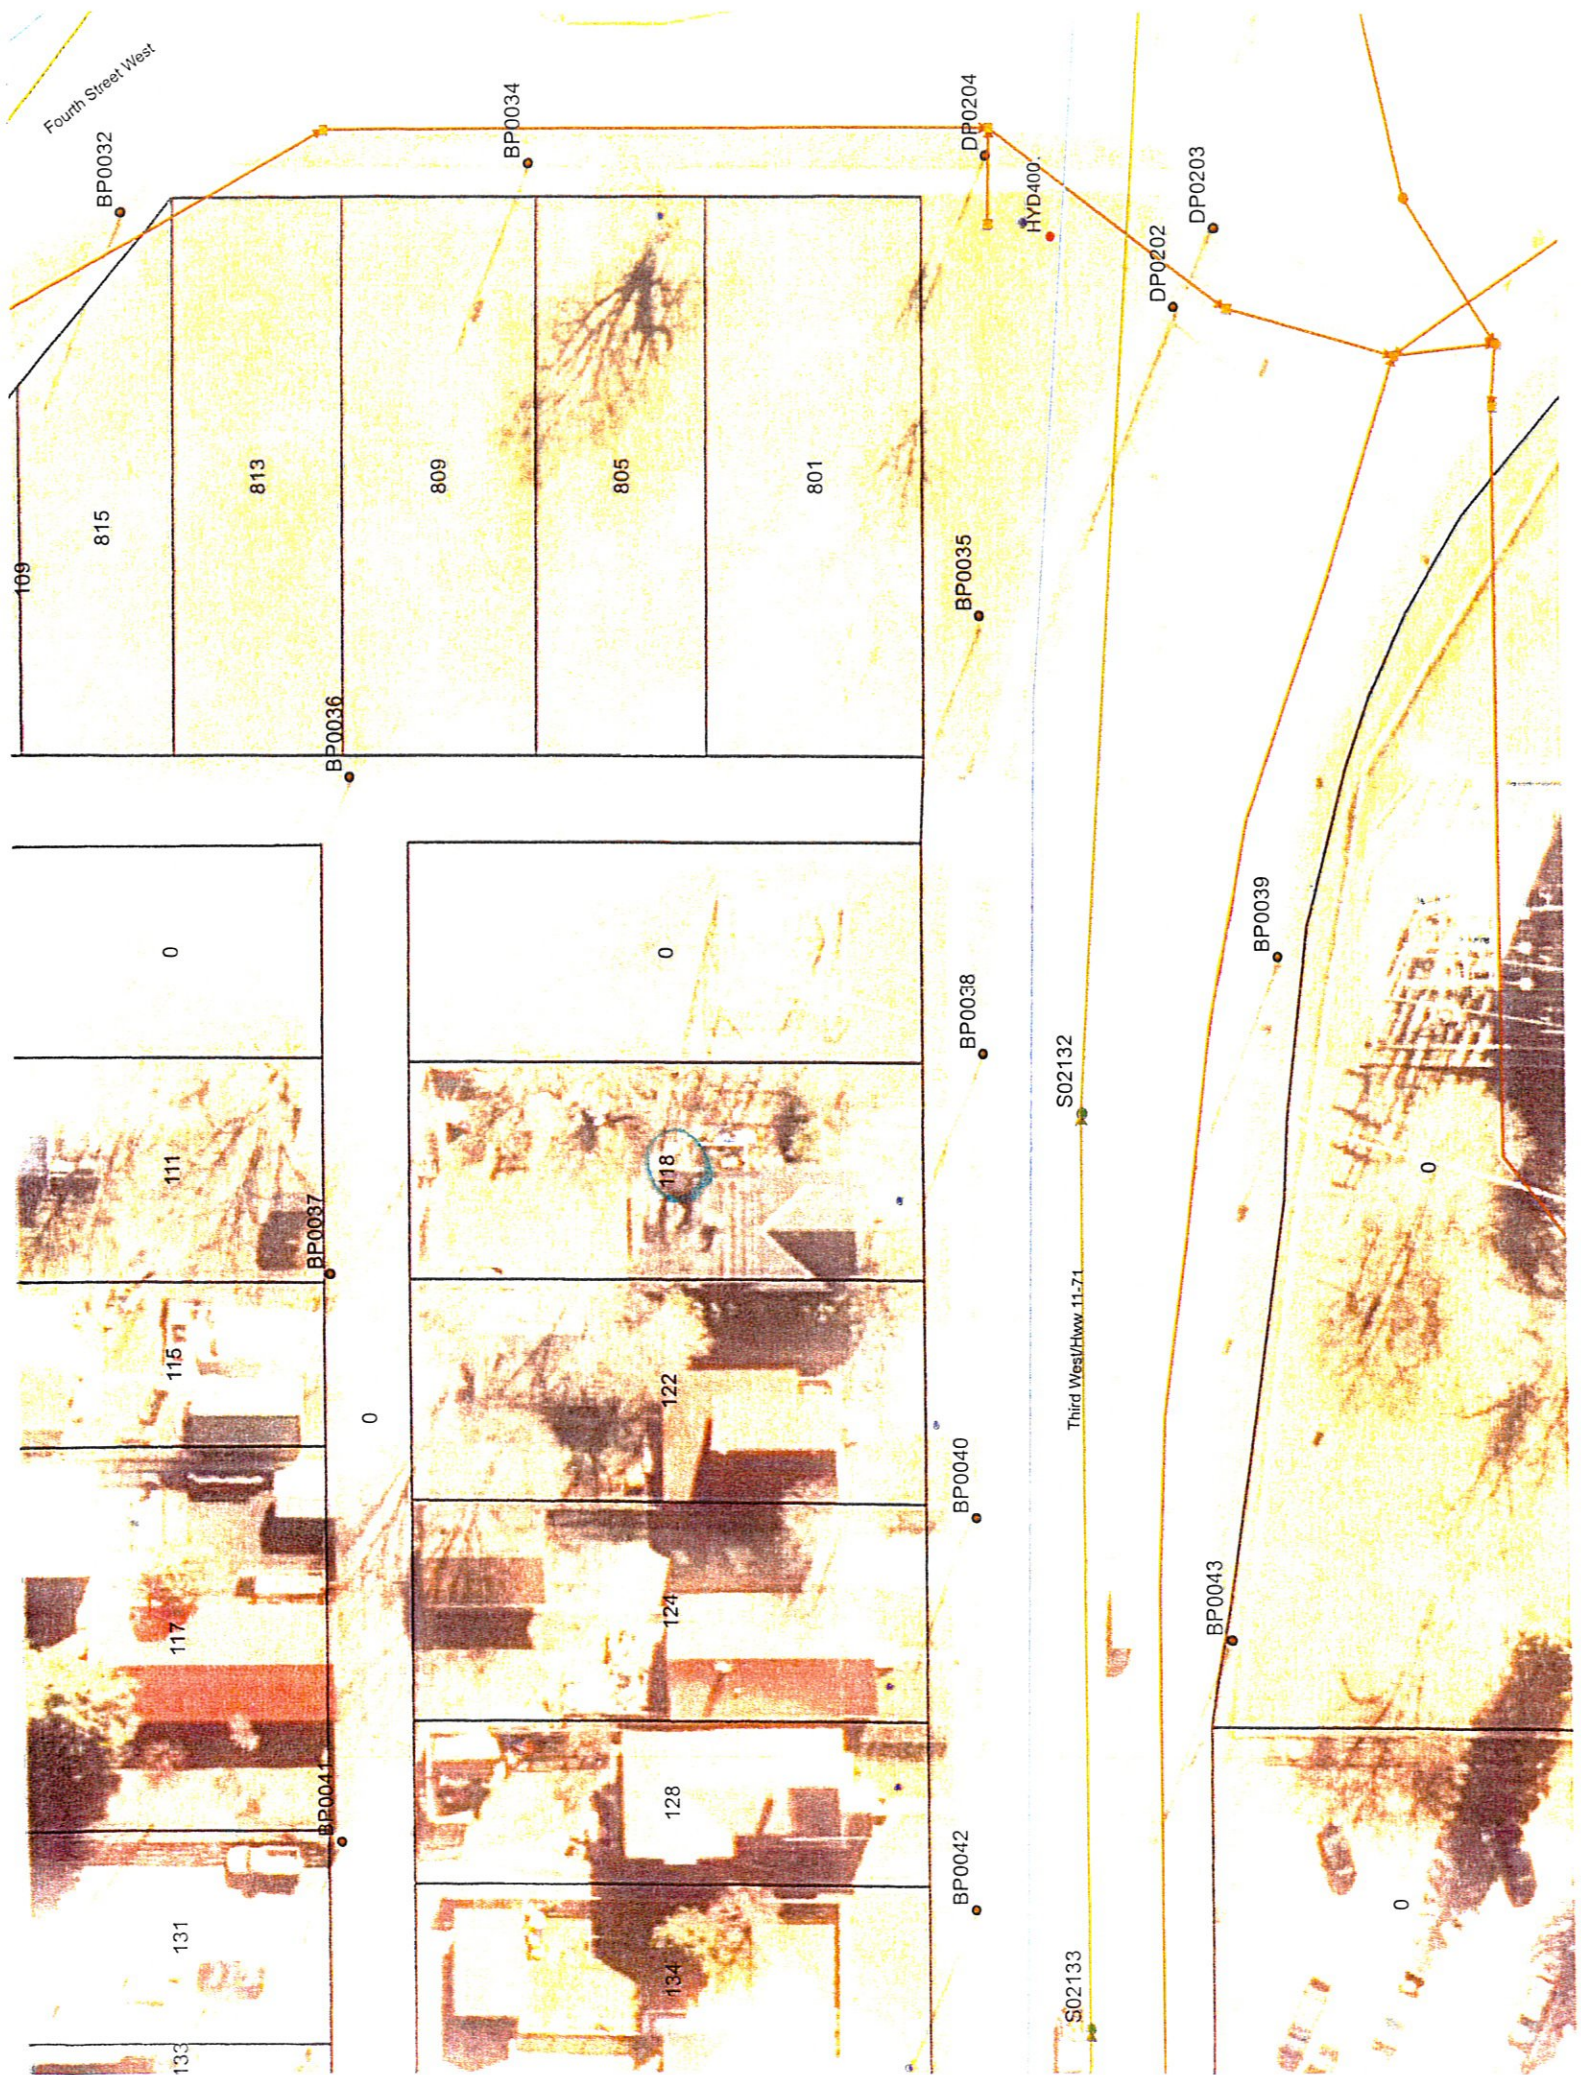

Fourth Street West

S02132

Third West/Hwy 11-71

S02133

109

815

813

809

805

801

0

111

115

117

131

133

BP00037

BP00041

0

0

118

122

124

128

134

BP00038

BP00040

BP00042

BP00035

BP00034

DP0204

HYD400

DP0202

DP0203

BP00043

BP00039

0

0
